



REVIEW OF MPLADS PROJECTS UNDER KENDRAPARA PARLIAMENTARY CONSTITUENCY 16th LOK SABHA

November - 2017

Total number of Projects – 163 Nos.
Total estimated investment in INR – 1,654.41 Lakhs.



Agency:-RWSS (KDP)

No. of Projects - 44

Estimated Investment in INR- 849.55
Lakhs.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Marshaghai.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP - Marshaghai
5. Block- Marshaghai

Status: -

- 1) Presently work in progress.
- 2) As reported by EE, expected date of completion - November 2017.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Andara.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP - Andara
5. Block- Pattamundai

Status: -

- 1) Presently work in progress.
- 2) As reported by EE, expected date of completion - January 2018.
(Earlier EDC was November 2017)



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Namtara.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP - Namtara

Status: -

- 1) Material mobilization process initiated.
- 2) As reported by EE, expected date of completion - December 2017.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Sansidha.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Sansidha
5. Block- Aul

Status:-

- 1) Work in progress.
- 2) As reported by EE, expected date of completion is April 2018.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Dholamara.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Dholamara
5. Block- Rainagar

Status:-

- 1) Work in progress.
- 2) As reported by EE, expected date of completion - December 2017.

All photographs taken by Team Jay Panda, report compiled by inputs from relevant authority, general public & site visit by Hon'ble MP and/or his team



Project Review November - 2017



Details:-


1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Gogua.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Gangapada
5. Block- Kendrapara

Status:-

- 1) Work in progress.
- 2) As reported by EE, expected date of completion is February 2018.



Project Review November – 2017

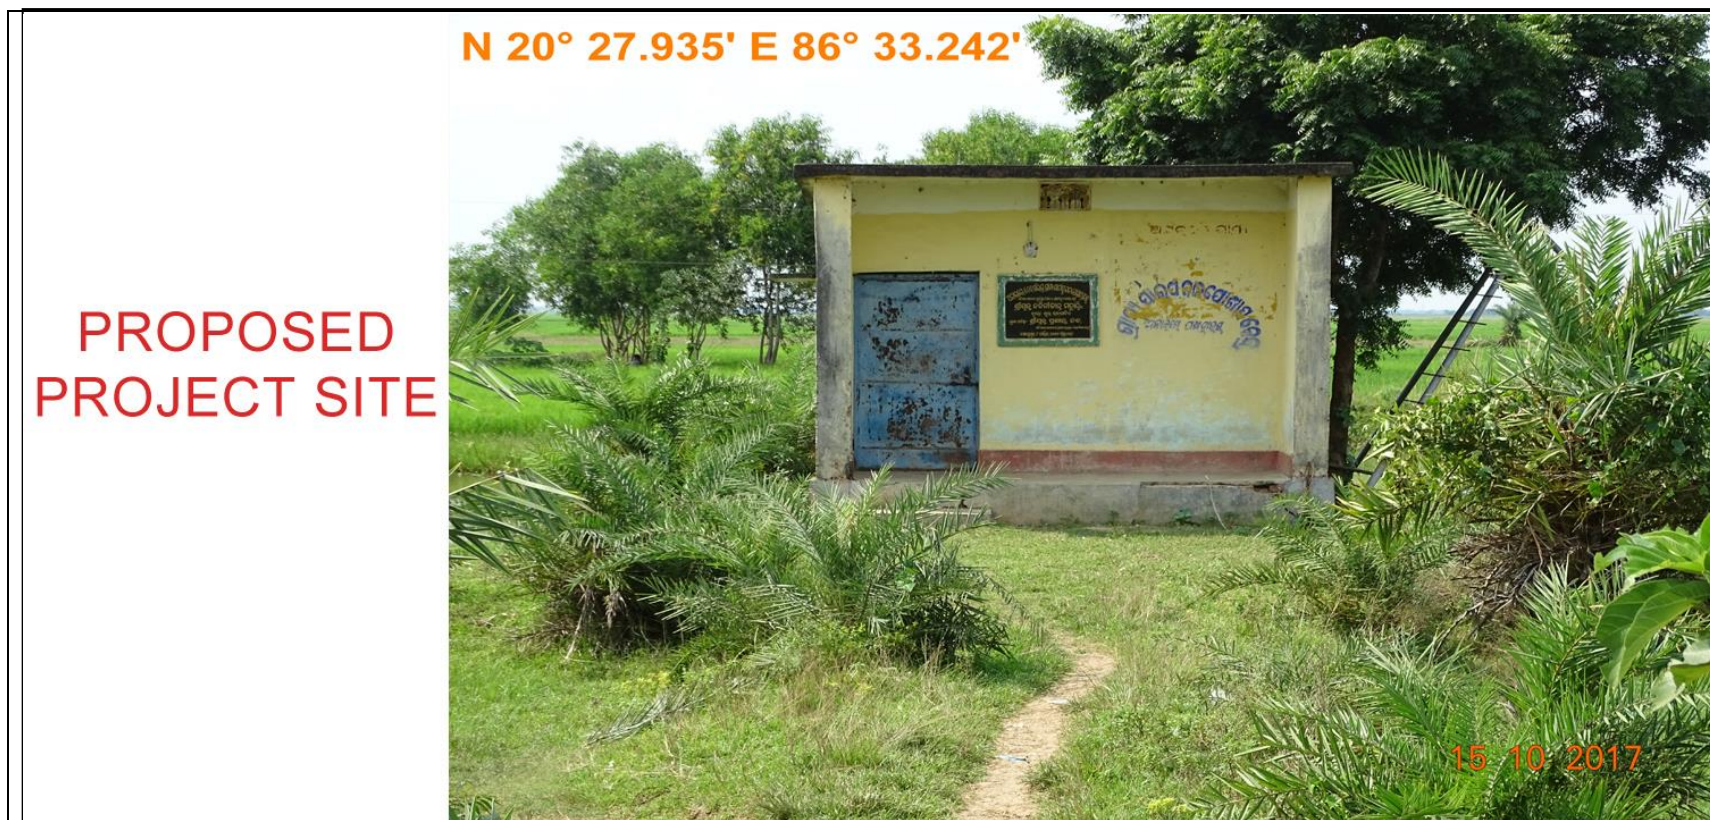

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Alailo.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP - Alailo
5. Block- Mahakalapada

Status: -

- 1) Tender process completed.
- 2) Soil test pending due to local dispute.
- 3) Concerned officials have been apprised to resolve the issues.



Project Review November - 2017

**PROPOSED
PROJECT SITE**



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Indalo.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Indalo
5. Block- Derabish

Status:-

- 1) Tender processing done.
- 2) As reported by EE, work will start soon.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Baradanga.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Baradanga
5. Block- Mahakalapada

Status:-

- 1) Tender processing done.
- 2) Soil test pending due to local dispute.
- 3) Concerned officials have been apprised to resolve the issues.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Jalapoka.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Jalapoka
5. Block- Marshaqhai

Status:-

- 1) Work just started after rainy season.
- 2) As reported by EE, expected date of completion is April 2018.



Project Review November – 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Kalagada.**
2. Investment in INR – 33.34 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Jadupur
5. Block- Mahakalapada

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Bangalpur.**
2. Investment in INR – 30.80 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Garadpur
5. Block- Garadpur

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Harianka.**
2. Investment in INR – 30.70 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Harianka
5. Block- Derabish

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Manikunda.**
2. Investment in INR – 30.69 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Manikunda
5. Block- Marshaghai

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Belapala.**
2. Investment in INR – 28.35 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Ostia
5. Block- Rajnagar

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Olaver.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Olaver
5. Block- Rajkanika

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Pachhapada.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Narsinghpur
5. Block- Pattamundai

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Demal.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Demal
5. Block- Aul

Status:-

- 1) Estimate submitted at District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Chandibaunsamul (Adjacent to Matia Mangala Temple).**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Chandibaunsamul
5. Block- Rajnagar

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Manikpatna.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Manikpatna
5. Block- Aul

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Raghudeipur.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Raghudeipur
5. Block- Derabish

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Ayitpur.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Ayitpur
5. Block- Marshaqhai

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Taradipal.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Taradipal
5. Block- Pattamundai

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Dhumat.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Dhumat
5. Block- Kendrapara

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Achyutipur.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Bharigada
5. Block- Rajkanika

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Koudiabarei.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Ramachandrapur
5. Block- Garadpur

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Kalapada.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Kalapada
5. Block- Kendrapara

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Talakusuma.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Talakusuma
5. Block- Garadpur

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Patalipanka.**
2. Investment in INR – 28.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Patalipanka
5. Block- Mahakalapada

Status:-

- 1) Estimate under process by govt. authorities.



Small Drinking Water Projects

Sl. #	Name of the Project	Cost of Project in Lakhs	Status as on Date
1	Installation of Tube well at Bhopal (Near house of Prafulla Das) under G.P.- Gogua Block- Mahakalpada	2.58	Funds awaited
2	Installation of Tube well at Kolanai Bandha Sahi (Near house of Keshab Chandra Bhola) Badihi GP under Mahakalapada block.	2.51	Funds awaited
3	Installation of Tube well at Jenapatna Dalit basti AT/GP- Damarpur under Pattamundai block.	2.48	Funds awaited
4	Installation of Tube well in front of AnjanNayak, Ward No-1, at Panchanapada of Sanamanga G.P of Aul block.	2.27	Funds awaited
5	Provision of one tube well in front of S.N. College, Rajkanika, Rajkanika Block	2.45	Dispute pending
6	Installation of Tube well at Badagan (Near house of Suresh Swain) Ashram Balikuda under G.P.- Balikuda Block- Mahakalpada	1.50	Estimate Stage
7	Installation of Tube well at Dera near house of Gobinda Swain of Dera G.P under Rajnagar block.	1.50	Estimate stage
8	Installation of Tube well at Nuagaon near house of Fakir Sahani of Dera G.P under Rajnagar block.	1.50	Estimate stage



Small Drinking Water Projects

9	Provision of cold drinking water facilities in the premises of Gajeshwar Bidyapitha, AT/GP-Deulipada under Mahakalapada block.	1.50	Estimate stage
10	Installation of Tube well at Sabarpada, Lunimatia village of Barkanda G.P under Mahakalapda block.	1.50	Estimate stage
11	Installation of Tube well at Atharabatia near house of Sanatan Mallick of Narsinghpur G.P under Pattamundai block.	1.50	Estimate stage
12	Installation of Tube well at Atharabatia near house of Kalakar Mallick of Narsinghpur G.P under Pattamundai block.	1.50	Estimate stage
13	Installation of Tube well at Ward No.8 near Badapokhari middle portion of the sahi Mangalpur G.P under Mahakalapada block.	1.41	Sanctioned
14	Installation of Tube well at Ward No.9 near Hanuman Temple, Mangalpur G.p under Mahakalpada block.	1.41	Sanctioned
15	Installation of Tube well at Ward No.10 near house of Akhaya Swain (middle portion of the sahi) Mangalpur G.P under Mahakalapada block.	1.41	Sanctioned



Agency:-RWSS (CUTTACK)

No. of Projects- 62

Estimated Investment in INR- 356.21
Lakhs.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Jaripada.**
2. Investment in INR – 25.23 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Jaripada
5. Block- Tangi-Choudwar

Status:-

- 1) Tender process completed.
- 2) As reported by EE, now rectification work started for failure source.



Project Review November - 2017



Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Mahajanpur**
2. Investment in INR – 25.23 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Mahajanpur
5. Block- Saliupur

Status:-

- 1) Tender process completed.
- 2) As reported by EE, work will start soon.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Asureswar.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Assureswar
5. Block- Nischintakoili

Status:-

- 1) Estimate received at district planning office, Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Sindhupur.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Podamarai
5. Block- Mahanga

Status:-

- 1) Estimate received at district planning office, Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Uchhapada.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Uchhapadxa
5. Block- Tangi-Choudwar

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Atoda.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Madhyakachha
5. Block- Salipur

Status:-

- 2) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Kanheipur.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Kanheipur
5. Block- Tangi-Choudwar

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Dharmagatpur.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Mirzapur
5. Block- Salipur

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Osanga.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Osanga
5. Block- Mahanga

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Patapur.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Jiginpur
5. Block- Nischintakoili

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Lalitgiri.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Lalitgiri
5. Block- Mahanga

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Katarpada.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Katarpada
5. Block- Nischintakoili

Status:-

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of ROT (Rural Overhead Tank) on existing RPWS scheme at Kolanpur.**
2. Investment in INR – 24.00 Lakhs
3. Agency – EE, RWSS
4. Vill / GP – Kolanpur
5. Block- Nischintakoili

Status:-

- 1) Estimate under process by govt. authorities.



Small Drinking Water Projects

SL #	Name of the projects	Cost in Lacs	Status as on Date
1	Installation of Tube-well to be fully completed at KetakiJhara (Mania), in front of house of late Gopal Singh, G.P- Uchhapada under Tangi-Choudwar block.	1.00	Work in progress
2	Installation of Tube-well to be fully completed at Kayapalli (near house of BabuliDehuri) G.P- Uchhapada under Tangi-Choudwar block.	1.00	Completed
3	Installation of Tube-well in Panchayat High School to be fully Completed At/GP-Kundi, Block -Mahanga, Dist-Cuttack	0.85	Completed
4	Installation of Tube-well to be fully completed at Mallickpur, Ward No.9, GP-Kundi, Block -Mahanga, Dist-Cuttack.	0.85	Sanctioned
5	Installation of Tube-well to be fully completed at Gunisahi, GP-Kaitha , Block - Mahanga, Dist-cuttack	0.85	Completed
6	Installation of Tube-well to be fully completed near Budhijagulai Pitha, ward No.-11, GP-Kuhunda, Block-Mahanga, Dist-Cuttack	0.85	Completed
7	Installation of Tube-well to be fully completed near Shyamasundarpur Pitha, Ward No.11, GP-Kuhunda , Block , Mahanga, Dist-Cuttack	0.85	Sanctioned
8	Installation of Tube-well Installation of Tube-well to be fully completed near Hata ,GP -Kuhunda, Block - Mahanga, Dist-cuttack	0.85	Sanctioned
9	Installation of Tube-well to be fully completed at MuslimBasti, Ward No.12, GP-Kuhunda,Block - Mahanga, Dist -Cuttack.	0.85	Completed
10	Installation of Tube-well to be fully completed at Beherasahi, Ward No.13GP-Kuhunda, Block-Mahanga, Dist-cuttack.	0.85	Sanctioned
11	Installation of Tube-well to be fully completed at Mallipura, Ward No.13, GP-Jaleswarpur, Block-Mahanga, Dist-cuttack	0.85	Sanctioned
12	Installation of Tube-well to be fully completed at Dharamdaspur Khandialisahi, GP-Mulabasant, Block-Mahanga , Dist -Cuttack	0.85	Sanctioned



Small Drinking Water Projects

13	Installation of Tube-well to be fully completed at Biswanathpur Bunakarsahi,GP-Jaripada, Block:Tangi-Choudwar, Dist-Cuttack	0.85	Completed
14	Installation of Tube-well to be fully complete at Biswanathpur Brahamanasahi , GP-Jaripada, Block:Tangi-Choudwar, Dist-Cuttack.	0.85	Completed
15	Installation of Tube-well to be fully completed at Saino Musalmansahi, GP- Napanga, Block, Tangi-Choudwar, Dist-Cuttack.	0.85	Sanctioned
16	Installation of Tube-well to be fully completed at Narapada Musalmansahi, GP -NapangaBlock:Tangi - Choudwar, Dist-Cuttack.	0.85	Sanctioned
17	Installation of Tube-well to be fully completed at Banika near School, GP Napanga, Block:Tangi - Choudwar, Dist-Cuttack.	0.85	Completed
18	Installation of Tube-well to be fully completed at Nadikula, Ward No-3, GP Jaripada, Block:Tangi - Choudwar, Dist-Cuttack.	0.85	Sanctioned
19	Installation of Tube-well to be fully completed at Charigharia, Ward No-11, GP -Kanheipur , Block :Tangi -Choudwar, Dist-Cuttack	0.85	Completed
20	Installation of Tube-well to be fully completed at Dhanabeni (near House of Sana Hembram) GP - Kanheipur , Block :Tangi -Choudwar, Dist-Cuttack.	0.85	Sanctioned
21	Installation of Tube-well to be fully completed at Chintamanipur Sarbar Sahi, GP-Kanheipur, Block:Tangi-Choudwar, Dist-Cuttack.	0.85	Completed
22	Installation of Tube-well to be fully completed at Urala Sahi, GP-Jaripada, Block:Tangi-Choudwar, Dist-Cuttack.	0.85	Sanctioned
23	Installation of Tube-well to be fully completed at Musalmansahi, GP-Jaripada, Block:Tangi-Choudwar, Dist-Cuttack.	0.85	Completed
23	Installation of Tube-well to be fully completed at Saranga,GP-Jaripada, Block: Tangi-Choudwar, Dist-Cuttack.	0.85	Completed
24	Installation of Tube-well to be fully completed at Bada Mohantysahi, GP-Jaripada, Block: Tangi-Choudwar, Dist-Cuttack.	0.85	Completed



Small Drinking Water Projects

25	Installation of Tube-well to be fully completed at Samantarapur (near house of Mr.Subas Jena), GP-Jaripada under Tangi-Choudwar Block, Dist-Cuttack.	0.85	Completed
26	Installation of Tube-well to be fully completed at Samantarapur (near house of Mr.ChakradharOjha), GP-Jaripada under Tangi-Choudwar Block, Dist-Cuttack.	0.85	Completed
27	Installation of Tube-well to be fully completed at JagannathHarijanSahi (near AWC) GP-Madhyakachha under Salipur Block, Dist-Cuttack	0.85	Completed
28	Installation of Tube-well to be fully completed at Jagannath (near house of Mr.Sanatan Das Gahamakuda) GP-Madhyakachha under Salipur Block, Dist-Cuttack	0.85	Completed
29	Installation of Tube-well to be fully completed at Ward No.10, Village-Purbakachha(near house of Mr.BishnuBhoi) GP-Madhyakachha under Salipur Block, Dist-Cuttack	0.85	Completed
30	Installation of Tube-well to be fully completed at Tarenigada, GP-Tarito under Salipur Block, Dist-Cuttack	0.85	Completed
31	Installation of Tube-well to be fully completed at Kharipadia Gada,Village/GP-Sudukhanda under Salipur Block, Dist-Cuttack	0.85	Completed
32	Installation of Tube-well to be fully completed at Ward No.11, Pati Sahi, Village-Kusunpur, GP-Jaripada under Tangi-Choudwar Block, Dist-Cuttack	0.85	Completed
33	Installation of Tube-well to be fully completed at Bhagabatpur , (near house of Mr.Prahallad Jena) village - Totasahi ,GP-jaripada under Tangi-Choudwar Block, Dist-Cuttack	0.85	Completed
34	Installation of Tube-well to be fully completed at Ward No.3 Nayak Sahi, village/GP-Madhyakachha under Salipur Block, Dist-Cuttack.	0.85	Completed



Small Drinking Water Projects

35	Installation of Tube-well to be fully completed at BaulaKaibartaSahi, Village /GP-Kaitha under Mahanga Block, Dist-Cuttack	0.85	Completed
36	Installation of Tube-well to be fully completed at Gokulapur (near house of Khirod Sahu), Village/GP-Gobindapur under Tangi-Choudwar Block, Dist-Cuttack.	0.85	Sanctioned
37	Installation of Tube-well to be fully completed at Ward No.3 Harijansahi, Village/GP-Jaleshwarpur under Mahanga Block, Dist-Cuttack.	0.85	Completed
38	Installation of Tube-well to be fully completed Jaleshwarpur (near G.P. office) under Mahanga Block, Dist-Cuttack	0.85	Completed
39	Installation of Tube-well to be fully completed at ward No.14, HarijanSahi, Village/GP-Narada under Salipur Block, Dist-Cuttack	0.85	Completed
40	Installation of Tube-well to be fully completed at Ward No.15 (near house of Bijaya Swain), Village/GP-Narada under Salipur Block, Dist-Cuttack	0.85	Completed
41	Installation of Tube-well to be fully completed at Samantarapur (Near AkshyaThakurani), GP-jaripada under Tangi-Choudwar Block, Dist-Cuttack	0.85	Completed
42	Installation of Tube-well to be fully completed at Dihakunda (near house of Mr.Bira Khuntia), Village/GP-Harianta under Tangi-Choudwar Block, Dist-Cuttack.	0.85	Sanctioned
43	Installation of Tube-well to be fully completed at Kharadasahi (near house of Mr.Kailash Chandra Sahani), Village/ GP-Harianta under Tangi-Choudwar Block, Dist-Cuttack	0.85	Completed



Small Drinking Water Projects

44	Installation of Tube-well to be fully completed at Anasarpur(near house of Mr. Bata KrushnaSahu), GP-Asureswar under Nischintakoili Block, DistCuttack.	0.85	Completed
45	Installation of Tube-well to be fully completed at LokanathpurMalakudasahi, Village/GP-Kentalo under Nischintakoili Block, Dist-Cuttack	0.85	Completed
46	Installation of Tube-well to be fully completed at Ward No.4, Village-Kotpad, GP - Trilochanpur under Salipur Block, Dist-Cuttack.	0.85	Completed
47	Installation of Tube-well to be fully completed at Tarito Dolamunde, Village/GP- Tarito under Salipur Block, Dist-Cuttack.	0.85	Completed
48	Installation of Tube- well to be fully completed near Anganwadi Centre at Upara Dalit Sahi of Ward No. 5, Lalitgiri G.P. under Mahanga Block	0.85	Completed
49	Installation of Tube-well at Sardala plays Ground (adjacent to newly constructed mini stadium at Sardala) in Harianta G.P. of Tangi-Choudwar Block, Dist-Cuttack.	0.65	Sanctioned



Agency:-BDO (Cuttack)

No. of Projects- 20

Estimated Investment in INR-107.51
Lakhs



Project Review November - 2017



Details:-

- 1.Name- **Expansion of Gallery of existing Mini Stadium at Raghunathpur Bidyapitha Playground.**
2. Investment in INR – 24.51 Lakhs
3. Agency – BDO, Mahanga
4. Vill / GP - Kotapda
5. Block – Mahanga

Status: -

- 1) Presently work in progress.
- 2) As reported by BDO, Expected date of completion – December 2017. (Earlier EDC was Jun 2017)
- 3) Delay due to local political interference.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Bahugram (Degree) Collage at Bahadulapatna.**
2. Investment in INR – 05.00 Lakhs
3. Agency – BDO, Salipur
4. Village/GP- Bahugram
5. Block- Salipur

Status: -

- 1) Estimate submitted at district planning office, Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of Mini Multipurpose Community Hall at Bantala.**
2. Investment in INR – 05.00 Lakhs
3. Agency – BDO, Mahanga
4. Village/GP- Gopalpur
5. Block- Mahanga

Status: -

- 1) Estimate completed.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of Mini Multipurpose Community Hall at Purbakachha.**
2. Investment in INR – 05.00 Lakhs
3. Agency – BDO, Salipur
4. Village/GP- Madhyakachha
5. Block- Salipur

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of one new class room of Saraswati SishuMandir at Naiguan.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Nischintikoili
4. Village/GP- Daudpur
5. Block- Nischintakoili

Status: -

- 1) Estimate submitted at district planning office, Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of one new class room of Belabana U.P School at Aliara**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Mahanga
4. Village/GP- Podamarai
5. Block- Mahanga

Status: -

- 1) Feasibility report received at District planning office, kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Mahapurusha Arakhita Das at Haribhagabatpur.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Mahanga
4. Village/GP- Lalitagiri
5. Block- Mahanga

Status: -

- 1) Feasibility report received at district planning office, kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Raghunathjew Secondary School at Matiparilo.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Mahanga
4. Village/GP- Paikarapur
5. Block- Mahanga

Status: -

- 1) Feasibility report received at district planning office, kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Jagulai Girls High School at Manitri.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Salipur
4. Village/GP- Pikol
5. Block- Salipur

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of one new class room of Panchayat High School at Malasasan.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Salipur
4. Village/GP- Malasasan
5. Block- Salipur

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Laxmi Nrushinga High School at Purusottampur.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Salipur
4. Village/GP- Sisua
5. Block- Salipur

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of one new class room of Panchayat High School at Boili**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Salipur
4. Village/GP- Ratilo
5. Block- Salipur

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Anchalika Juniouir College at Reba.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Salipur
4. Village/GP- Rameswar
5. Block- Salipur

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Duryodhan Bidyapitha at Buhalo.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Nischintakoili
4. Village/GP- Buhalo.
5. Block- Nischintakoili

Status: -

- 1) Estimate/ feasibility report submitted at district planning office.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Balipada High School at Balipada.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Nischintakoili
4. Village/GP- Balipada
5. Block- Nischintakoili

Status: -

- 1) Estimate/ feasibility report submitted at district planning office.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of one new class room of Lalbag Girls High School at Jiginpur.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Nischintakoili
4. Village/GP- Jiginpur
5. Block- Nischintakoili

Status: -

- 1) Estimate/ feasibility report submitted at district planning office.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name-**Construction of one new class room of Kasi Dulali Girls High School at Tarat.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Nischintakoili
4. Village/GP- Tarat
5. Block- Nischintakoili

Status: -

- 1) Estimate/ feasibility report submitted at district planning office.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of one new class room of Shakuntala Vidyaniketan at Bodhanga.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Nischintakoili
4. Village/GP- Doudpur
5. Block- Nischintakoili

Status: -

- 1) Estimate/ feasibility report submitted at district planning office.
- 2) Awaited funds to sanction the same.



Project Review November – 2017

SL #	Name of the projects	Cost in Lacs	Status as on Date
1	Completion of class room of Biswanahakani Mahavidyalaya at Biswanahakani under Garudagaon G.P of Tangi-Choudwar block.	3.00	Land details awaited.
2	Completion of class room of LP School at Napatua under Garudagaon G.P of Tangi-Choudwar block.	2.00	Land details awaited.



Agency:-Municipality (KDP)

No. of Projects- 07

Estimated Investment in INR- 50.00 Lakhs



Project Review November - 2017



Details:-

- 1.Name- **Construction of Science Laboratory and Library of Bharati Vidya Mandir.**
2. Investment in INR – 15.00 Lakhs
3. Agency – EO, Municipality, Kendrapara
4. Municipality - Kendrapara

Status: -

- 1) As reported by Executive Officer, work will start soon.



Project Review November - 2017



Details:-

- 1.Name- **Construction of new class room of Sri Aurobindo Integral Education Centre at Mirpatna.**
2. Investment in INR – 04.50 Lakhs
3. Agency – EO, Municipality, Kendrapara
4. Municipality - Kendrapara

Status: -

- 1) Presently work in progress.
- 2) As reported by Executive Officer, expected date of completion November 2017.



Project Review November - 2017

**PROPOSED
PROJECT SITE**



Details:-

1. Name- **Construction of SCT (Smart Community Toilet) at sweeper colony ward # 13.**
2. Investment in INR – 07.00 Lakhs
3. Agency – EO, Municipality
4. Municipality – Ward # 13

Status: -

- 1) Project sanctioned.
- 2) As reported by Executive Officer, work will start soon.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of two new classrooms of Al-Farooque Educational Trust at Mehemoodabad.**
2. Investment in INR – 09.00 Lakhs
3. Agency – EO, Municipality
4. Municipality – Mehemoodabad

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of burning platform in existing cremation shed and boundary wall at Meghabarada.**
2. Investment in INR – 05.00 Lakhs
3. Agency – EO, Municipality, Kendrapara
4. Municipality - Kendrapara

Status: -

- 1) Estimate under process by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of boundary wall of Quadeem Basti at Goudapada**
2. Investment in INR – 05.00 Lakhs
3. Agency – EO, Municipality, Kendrapara
4. Municipality - Kendrapara

Status: -

- 1) Estimate submitted to DPMU Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of new classrooms of Madrasa Arabia Talimul Islam at Badahat.**
2. Investment in INR – 04.50 Lakhs
3. Agency – EO, Municipality, Kendrapara
4. Municipality - Kendrapara

Status: -

- 1) Estimate under process by govt. authorities.
- 2) Awaited funds to sanction the same.



Agency:-Rural Works Division-II (KDP)

No. of Projects- 02

Estimated Investment in INR-56.93 Lakhs



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of Mini Stadium at Shri Jagannath High School Playground.**
2. Investment in INR – 35.17 Lakhs
3. Agency – EE, Rural Works- II
4. Village/GP- Keredagarh
5. Block- Rajnagar

Status: -

- 1) Estimate submitted with District Planning Office, Kendrapara.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of Multipurpose building at Penthapal.**
2. Investment in INR – 21.76 Lakhs
3. Agency – EE, Rural Works- II
4. Village/GP- Penthapal
5. Block- Pattamundai

Status: -

- 1) Estimate submitted at DPMU, Kdp.
- 2) Awaited funds to sanction the same.



Agency:-Rural Works Division (Cuttack)

No. of Projects- 02

Estimated Investment in INR-55.70 Lakhs



Project Review November - 2017



Details:-

1. Name- **Construction of Mini Stadium at Sidhagiri Bidyapitha Playground.**
2. Investment in INR – 27.85 Lakhs
3. Agency – EE, RWD-I, Division.
4. Vill / GP - Govindpur
5. Block – Tangi-Choudwar

Status: -

- 1) Presently work in progress.
- 2) As reported by EE, expected date of completion is December 2017.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name-**Construction of Mini Stadium at Choudhury Radhanath Bidyapitha Playground.**
2. Investment in INR – 27.85 Lakhs
3. Agency – EE, RWD-I, Division.
4. Vill / GP - Bhera
5. Block - Mahanada

Status: -

- 1) As reported by EE, cancellation of project in process due to technical reasons.



Agency:-BDO (KDP)

No. of Projects- 15

Estimated Investment in INR-55.50 Lakhs



Project Review November - 2017



Details:-

1. Name- **Construction of Regional Pensioners Association hall at Mahala.**
2. Investment in INR – 10.00 Lakhs
3. Agency – BDO, Garadpur
4. Vill / GP - Bangalpur
5. Block – Garadpur

Status: -

- 1) Work completed in all respect.
- 2) Shift this page to completed section.





Project Review November - 2017



Details:-

1. Name- **Construction of Rest shed for parents at Jawahar Navodaya Vidyalaya.**
2. Investment in INR – 05.50 Lakhs
3. Agency – BDO, Kendrapara
4. Village/GP- Baro
5. Block- Kendrapara

Status: -

- 1) Work in progress.
- 2) As reported by BDO, expected date of completion is March 2018.



Project Review November - 2017



Details:-

- 1.Name- **Construction of one class room of IslamiaJame-ulUloom at Jamadhar.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Kendrapara
4. Village/GP- Jamadhar
5. Block- Kendrapara

Status: -

- 1) Presently work stopped.
- 2) As reported by BDO, notice issued to the agency for early completion.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of boundary wall of Kalapahad Rasulpur Panchyat Kabarsthan at Rasulpur.**
2. Investment in INR – 05.00 Lakhs
3. Agency – BDO, Aul
4. Vill / GP - Rasulpur
5. Block – Aul

Status: -

- 1) Estimate submitted to DPMU, Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

- 1.Name- **Construction of boundary wall of Badabasti Choudakulat Kabarsthan at Choudakulat.**
2. Investment in INR – 05.00 Lakhs
3. Agency – BDO, Kendrapara
4. Vill / GP - Chandanpur
5. Block – Kendrapara

Status: -

- 1) Estimate submitted to DPMU, Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name-**Construction of new class room of Madrasa Zeenatul Quram at Nainipur, Tyendakuda.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Garadpur
4. Village/GP- Nainipur
5. Block- Garadpur

Status: -

- 1) Estimate submitted and land documents awaited to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of one new class room of Agni Kumari Nodal U.P School at Badihi.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Mahakalapada
4. Village/GP- Badihi
5. Block- Mahakalapada

Status: -

- 1) Estimate under progress by govt. authorities.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name-**Construction of one new class room of Adhakhanda Mathasahi U.G.M.E School at Adhakhanda Mathasahi.**
2. Investment in INR – 04.50 Lakhs
3. Agency – BDO, Kendrapara
4. Village/GP- Baro
5. Block- Kendrapara

Status: -

- 1) Estimate under progress by govt. authorities.



Project Review November - 2017

Sl. #	Name of the Project	Cost in Lakhs	Status as on Date
1	Construction of Mini Multipurpose Hall (Maa Sunamani GaonKalyan Samiti) at Jariabara of Bandhakata GP under Marshghai block.	3.00	Sanctioned
2	Completion of concrete cycle stand in the premises of Panchayat high school, AT/PO-Kalabuda	2.50	Funds awaited
3	Construction of boundary wall of Kabarstan at Patkura Muslim Bastee (Next to Patkura CHC) AT/GP – Patkura, Block-Garadpur	2.00	Funds awaited
4	Installation of one set of high mast light at DuhuriaChawk under Jamdhar GP of Kebdrapara block.	1.50	Funds awaited
5	Construction of cremation shed at Ainipada under Narsinghpur G.P of Pattamundai Block.	1.00	Funds awaited
6	Installation of one semi high mast light at Rajnagar CHC, AT/PO/Block-Rajnagar	1.00	Funds awaited
7	Construction of one toilet at Rajnagar CHC, AT/PO/Block- Rajnagar	1.00	Funds awaited



Agency:-Rural Works Division-I (KDP)

No. of Projects- 02

Estimated Investment in INR- 41.19Lakhs



Project Review November - 2017



Details:-

1. Name- **Construction of Multipurpose building at Tilakpur.**
2. Investment in INR – 26.19 Lakhs
3. Agency – EE, Rural Works, Division-I
4. Vill / GP - Tilakpur
5. Block- Derabish

Status: -

- 1) Work in progress.
- 2) As reported by EE, expected date of completion – December 2017.
(Earlier EDC was September 2017)



Project Review November - 2017



Details:-

1. Name- **Construction of Multipurpose hall at Sidhamarichini Bidyapitha, Bagada.**
2. Investment in INR – 15.00 Lakhs
3. Agency – EE, Rural Works, Division-I
4. Vill / GP - Bagada
5. Block- Kendrapara

Status: -

- 1) Work in progress.
- 2) As reported by EE, expected date of completion is June – 2018.



Agency:-Municipality Pattamundai (KDP)

No. of Projects- 05

Estimated Investment in INR-31.00 Lakhs



Project Review November - 2017



Details:-

1. Name- **Construction of one new class room of Pokhariapada Nodal U.P. School, AT- Pokhariapada, in Ward # 14**
2. Investment in INR – 06.02 Lakhs
3. Agency – EO, Municipality
4. Ward # - 12
5. Municipality - Pattamundai

Status: -

- 1) Work in progress.
- 2) As reported by EO, expected date of completion – November 2017.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of Multipurpose building in Ward # 12 at Baktarpur.**
2. Investment in INR – 12.00 Lakhs
3. Agency – EO, Municipality
4. Ward # - 12
5. Municipality - Pattamundai

Status: -

- 1) Estimate submitted at district planning office, Kdp.
- 2) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Construction of SCT (Smart Community Toilet) in Ward # 06**
2. Investment in INR – 07.00 Lakhs
3. Agency – EO, Municipality
4. Ward # - 06
5. Municipality - Pattamundai

Status: -

- 1) Estimate submitted at district planning office, Kdp.
- 3) Awaited funds to sanction the same.



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Completion of Kasturi Kalaniketan to be fully completed at Pokhariapada.**
2. Investment in INR – 04.50 Lakhs
3. Agency – EO, Municipality
4. Ward # - 14
5. Municipality - Pattamundai

Status: -

- 4) Estimate under progress by govt. authorities



Project Review November - 2017

SI. #	Name of the Project	Cost of Project in Lakhs	Status as on Date
1	Installation of one semi high mast light in Pattamundai CHC, Ward No. 14, Pattamundai Municipality	1.48	Completed



Agency:- Collector (KDP)

No. of Projects- 02

Estimated Investment in INR-23.10 Lakhs



Project Review November - 2017

PROPOSED PROJECT

Details:-

1. Name- **Purchase of two numbers of 20 seated FRP boat with 4 stroke Engine (25 HP).**
2. Investment in INR – 23.10 Lakhs
3. Agency – Collector
4. Block- Rajkanika

Status: -

- 1) Fund released to purchase the same.



Agency:-R&B (KDP)

No. of Projects- 01

Estimated Investment in INR-20.72 Lakhs



Project Review November - 2017



Details:-

- 1.Name- **Expansion of Gallery of existing mini stadium at M.N High School.**
2. Investment in INR – 20.72 Lakhs
3. Agency – EE, R&B- Kendrapara
4. Municipality - Pattamundai

Status: -

- 1) Civil portion completed and for finishing work additional estimate submitted to DPMU.
- 2) As reported by DD planning, some changes in estimate is required for which the same has been informed to concerned officials.



Agency:-CDMO (KDP)

No. of Projects- 01

Estimated Investment in INR-7.00 Lakhs




Project Review November - 2017



Details:-
1.Name- **Provision of one Hearse Van for District Headquarter Hospital.**
2. Investment in INR – 7.00 Lakhs
3. Agency – CDMO
4. District - Kendrapara

Status: -

1) Project completed/ dedicated to dist. Administration. 

2) Shift this page to completed section.
